First and Final Bill

M. A. R. 57 (Rule 116)
Measurement Book **No. B**

ial No. Improvements to Drains at Kuvempu layout Kempapura 501386
ne of Work in ward No. 07. Byrathayanapura. From ..... To .....
ne of Contractor of nature of Agency Sri Siddartha, Contractor, Banglore-32.
e of commencement of work 30/07/2022

te	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
	Est cost:	Rs. 15.00 lakhs					
	Job code:	007-22-000012 P3726					
	Work order:	BBMP/EE/BTP/WO/23/2022-23 Dt: 22/04/2022.					
1)	Earthwork excavation by manual means in ordinary soil throwing an average horizontal throw up to 2m and an average lift up to 1.5m excavated surface as per Sl. No. 1 in Schedule F-HB page No. 1 @ Rs. 118.00/cum					222.75 cum	26285=00

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	
	2) Providing and laying in position plain cement concrete of mix 1:3:6 with OPC @ 220 kgs with crushed 40mm and down size graded granite						
	Qty vide E-MB page no.] is					29.88 m³	45173
	@Rs. 5078.00/m³						
	3) Providing and laying in plain reinforced cement concrete mix 1:2:4 with OPC @ 240 kgs with 40mm and down size graded granite						
	Qty vide E-MB page no. 2 is					47.03 m³	240088
	@Rs. 5105.00/m³						

M. A. R. 57 (Rule 116)
Measurement Book

No. B

501387

Measl No. .....

e of Work ..... From..... To.....

e of Contractor of nature of Agency .....

of commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
4) Providing THT Steel reinforcement for R.C.C work including straightening, cutting, bending, bodding, Placing in position lapping and/or welding as per Mch E.M.S page no. 3 is					2.35 Tonnes	
@ Rs. 77912.00/ Tonnes						183093:00
5) Providing and removing centering, shuttering, strutting propping etc for columns, pillars, piers abutment Pier and struts, square/rectangular slabs						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	
	Aby vide E-MB Page no. 3 is					796.80 m2	
	@Rs. 415.00/m2						330672
6)	Providing and fixing 10cms thick pre cast RCC covering Slabs using reinforced cement concrete M20 mix with Stone aggregates 20mm and down size						
	Aby vide E-MB Page no. is 3					99.60 m2	
	@Rs 2009.00/m2						200096
7)	Loading and unloading of stones boulders/ stone aggregates / sand / kankar / moorum placing tipper at loading point loading with both end loading						

M. A. R. 57 (Rule 116)
Measurement Book

No. B 501388

No. .....

of Work ..... From..... To.....

of Contractor of nature of Agency .....

f commencement of work .....

Full description, etc, of work 2	Dimensions				Contents 7	Reference to last Measurement 8
	Number 3	Length 4	Breadth 5	Depth 6		
Qty vide E-MB Pageno. 3 is					222.75 m³	
@Rs. 81.00/m³						18043=00
Sub total						1150008=00
GST @ 12%						138001=00
Grand total						1288,009=00
					Round off.	12,88,000.00

30/07/18 Assistant Executive Engineer
Kodigehalli Sub Division

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents
		Number	Length	Breadth	Depth	
1	2	3	4	5	6	7

Certificate:-

1. Certified that the contractor done the work satisfactorily.
2. Certified that the contractor has clear all the debris from the work spot.
3. Certified that there is no departmental issues with the contractor.

30/07/22

Siddesh
Contractor

30/07

Assistant Executive Engir
Kodigehalli Sub Divisi
BBMP, Bangalore

Contents

7

M. A. R. 57 (Rule 116)
Measurement Book

No. B 501389

lo. .....

f Work ..... From..... To.....

f Contractor of nature of Agency .....

commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8

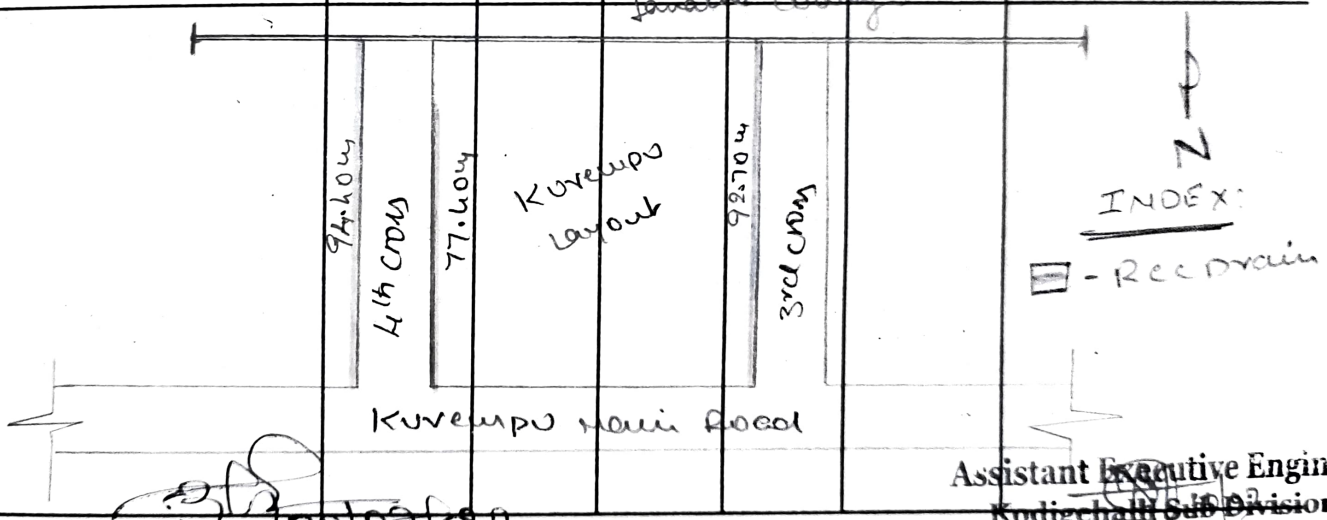

30/07/22

Assistant Executive Engineer
Kodigehalli Sub Division
BBMP, Bangalore

1st & Final

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents
		Number	Length	Breadth	Depth	
1	2	3	4	5	6	7
	Escrow Account P 3726					
	ಲಕ್ಷ್ಮೀಪುರಕ್ಕೆ Zonal Public Works - Pow Works ರವರಿಗೆ ಒಟ್ಟು ಮೊಬಲಗು ರೂ. 12,88,000/- ಗಳನ್ನು ಪಾಸು ಮಾಡಿದೆ ಇದರಲ್ಲಿ ರೂ. 1,28,000/- ಗಳನ್ನು ಜೊಂದಾಣಿಕೆ ಮಾಡಿಕೊಂಡು ರೂ. 11,60,000/- ಗಳನ್ನು		TTB	12,88,000.00		1st & final
			It	12,880.00		
			CGST	11,500.00		
			SGST	11,500.00		
			FSD	64,400.00		
			CESS	12,880.00		
			CBR	1,288.00		
			LR	12,652.00		
			Fine	900.00		
			Ded :	1,28,000.00		
			Net Payable	11,60,000.00		
	FT/REPT/KTOS ಮುಂಬಾಕಿ ಇರುವುದಿಲ್ಲ ಸಹಿ ಜೂನಿಯರ್ ಇಂಜಿನಿಯರ್ ಸಹಾಯಕ ಇಂಜಿನಿಯರ್ 24/9/22					
